



St. Bernard Parish Government

8201 West Judge Perez Drive
Chalmette, Louisiana 70043
504-278-4331 504-278-4330(fax)

Guy McInnis
Parish President

REQUEST FOR VIEWING AND/OR RECEIVING PUBLIC RECORDS

Name: Floyd Lachney, Jr.
Project Manager, Hamp's Const. Date: 6-17-16

Phone No. 504-342-6987 Email Address: FLJ@hampconstruction.com

Address: 1319 Newton St. New Orleans, LA 70114
Street City/State Zip Code

Records Requested:

Please See Attachment !

I agree to pay up to \$ Full Amount for the information requested.

I will pick up documents: I prefer documents to be mailed:
(Additional charges applies)

FOR OFFICE USE ONLY:

Date request received by SBPG: _____

Date records received by Requester: _____ Cost: \$ _____

Payment Method: Check Money Order

NOTE:

Anyone requesting records are required to pay \$.25 per page after the first four (4) pages and an additional \$1.00 per page for faxed documents. (Payment must be paid prior to receiving fax or mailed documents).

Send completed form to stank@sbpg.net or fax to 504-278-4330.

Public Records Request

Attachment 1

Please provide the name of the person or firm that produced the meeting minutes for the mandatory pre bid conference for the PALMISANO BOULEVARD DRAINAGE REPAIRS AND IMPROVEMENTS project that bid on May 10, 2016.

Did that person use an audio recording device to assist in the production of the minutes?

If so, we would like a copy of the recording.

If anyone else is in possession of an audio recording of the meeting, we would like a copy of that recording.


ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	3rd Quarter					4th Q
								May	Jun	Jul	Aug	Sep	
1		Palmisano Drainage Improvement	287 days	Mon 8/1/16	Tue 9/5/17								
2		Notice to Proceed	0 days	Mon 8/1/16	Mon 8/1/16								
3		Mobilization / Assembly Period	45 days	Mon 6/6/16	Fri 8/5/16								
4		Submittals	45 days	Mon 6/6/16	Fri 8/5/16								
5		Site Videos	30 days	Mon 6/20/16	Fri 7/29/16								
6		Engineering Layout	5 days	Mon 8/1/16	Fri 8/5/16	5							
7		Palmisano Bridge	109 days	Mon 8/1/16	Thu 12/29/16								
8		Mobilization	3 days	Mon 8/1/16	Wed 8/3/16								
9		Test Pile Program	15 days	Thu 8/4/16	Wed 8/24/16	8	BLD Bridge Crew						
10		Demolition	10 days	Thu 8/11/16	Wed 8/24/16	9SS+5 days	BLD Bridge Crew						
11		Bridge Work	60 days	Thu 8/25/16	Wed 11/16/16	9	BLD Bridge Crew						
12		Utility Work	15 days	Thu 11/17/16	Wed 12/7/16	11	BLD Bridge Crew						
13		Restoration Work	15 days	Thu 12/8/16	Wed 12/28/16	12	BLD Bridge Crew						
14		Final Inspection / Walk Through	1 day	Thu 12/29/16	Thu 12/29/16	13	BLD Bridge Crew						
15		10 x 6 Box Culvert Drainage	246 days	Mon 9/12/16	Mon 8/21/17								
16		Mobilization	1 day	Mon 9/12/16	Mon 9/12/16		BLD Drain Crew 1						
17		Clearing and Grubbing	3 days	Tue 9/13/16	Thu 9/15/16	16	BLD Drain Crew 1						
18		Utility Work	160 days	Fri 9/16/16	Thu 4/27/17	17	BLD Drain Crew 1						
19		Restoration Work	60 days	Fri 4/28/17	Thu 7/20/17	18	BLD Drain Crew 1						
20		Landscaping	20 days	Fri 7/21/17	Thu 8/17/17	19	BLD Drain Crew 1						
21		Final Inspection / Walk Through	2 days	Fri 8/18/17	Mon 8/21/17	20	BLD Drain Crew 1						
22		8 x 4 Box Culvert Drainage	211 days	Mon 11/14/16	Mon 9/4/17								
23		Mobilization	1 day	Mon 11/14/16	Mon 11/14/16	16SS+45 days	BLD Drain Crew 2						
24		Clearing and Grubbing	3 days	Tue 11/15/16	Thu 11/17/16	23	BLD Drain Crew 2						
25		Utility Work	130 days	Fri 11/18/16	Thu 5/18/17	24	BLD Drain Crew 2						
26		Restoration Work	55 days	Fri 5/19/17	Thu 8/3/17	25	BLD Drain Crew 2						
27		Landscaping	20 days	Fri 8/4/17	Thu 8/31/17	26	BLD Drain Crew 2						
28		Final Inspection / Walk Through	2 days	Fri 9/1/17	Mon 9/4/17	27	BLD Drain Crew 2						
29		Drainage Pump Station	39 days	Mon 1/2/17	Thu 2/23/17								
30		Mobilization	1 day	Mon 1/2/17	Mon 1/2/17		BLD Station Crew						
31		By-Pass System	3 days	Tue 1/3/17	Thu 1/5/17	30	BLD Station Crew						
32		Pile Work	3 days	Fri 1/6/17	Tue 1/10/17	31	BLD Station Crew						
33		Directional Drill	10 days	Wed 1/11/17	Tue 1/24/17	32	BLD Station Crew						
34		Excavate and Set Pump Station	5 days	Wed 1/25/17	Tue 1/31/17	33	BLD Station Crew						
35		Mechanical Work (Pumps and Piping)	10 days	Wed 2/1/17	Tue 2/14/17	34	BLD Station Crew						
36		Electrical Work	5 days	Wed 2/15/17	Tue 2/21/17	35	BLD Station Crew						
37		Final Inspection / Walk Through	2 days	Wed 2/22/17	Thu 2/23/17	36	BLD Station Crew						
38		Drainage Work Along St. Bernard Highway	18 days	Fri 2/24/17	Tue 3/21/17								
39		Mobilization	1 day	Fri 2/24/17	Fri 2/24/17	37	BLD Station Crew						
40		Clean Existing Drain Lines	5 days	Mon 2/27/17	Fri 3/3/17	39	BLD Station Crew						
41		Clean Existing Ditches	10 days	Mon 3/6/17	Fri 3/17/17	40	BLD Station Crew						

Project: Submitted Palmisano Dra
Date: Wed 5/18/16

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	3rd Quarter				4th Q	
								May	Jun	Jul	Aug		Sep
42		Final Inspection / Walk Through	2 days	Mon 3/20/17	Tue 3/21/17	41	BLD Station Crew						

Project: Submitted Palmisano Dra Date: Wed 5/18/16	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Progress	
	Milestone		External Milestone		Manual Task		Start-only			
	Summary		Inactive Task		Duration-only		Finish-only			

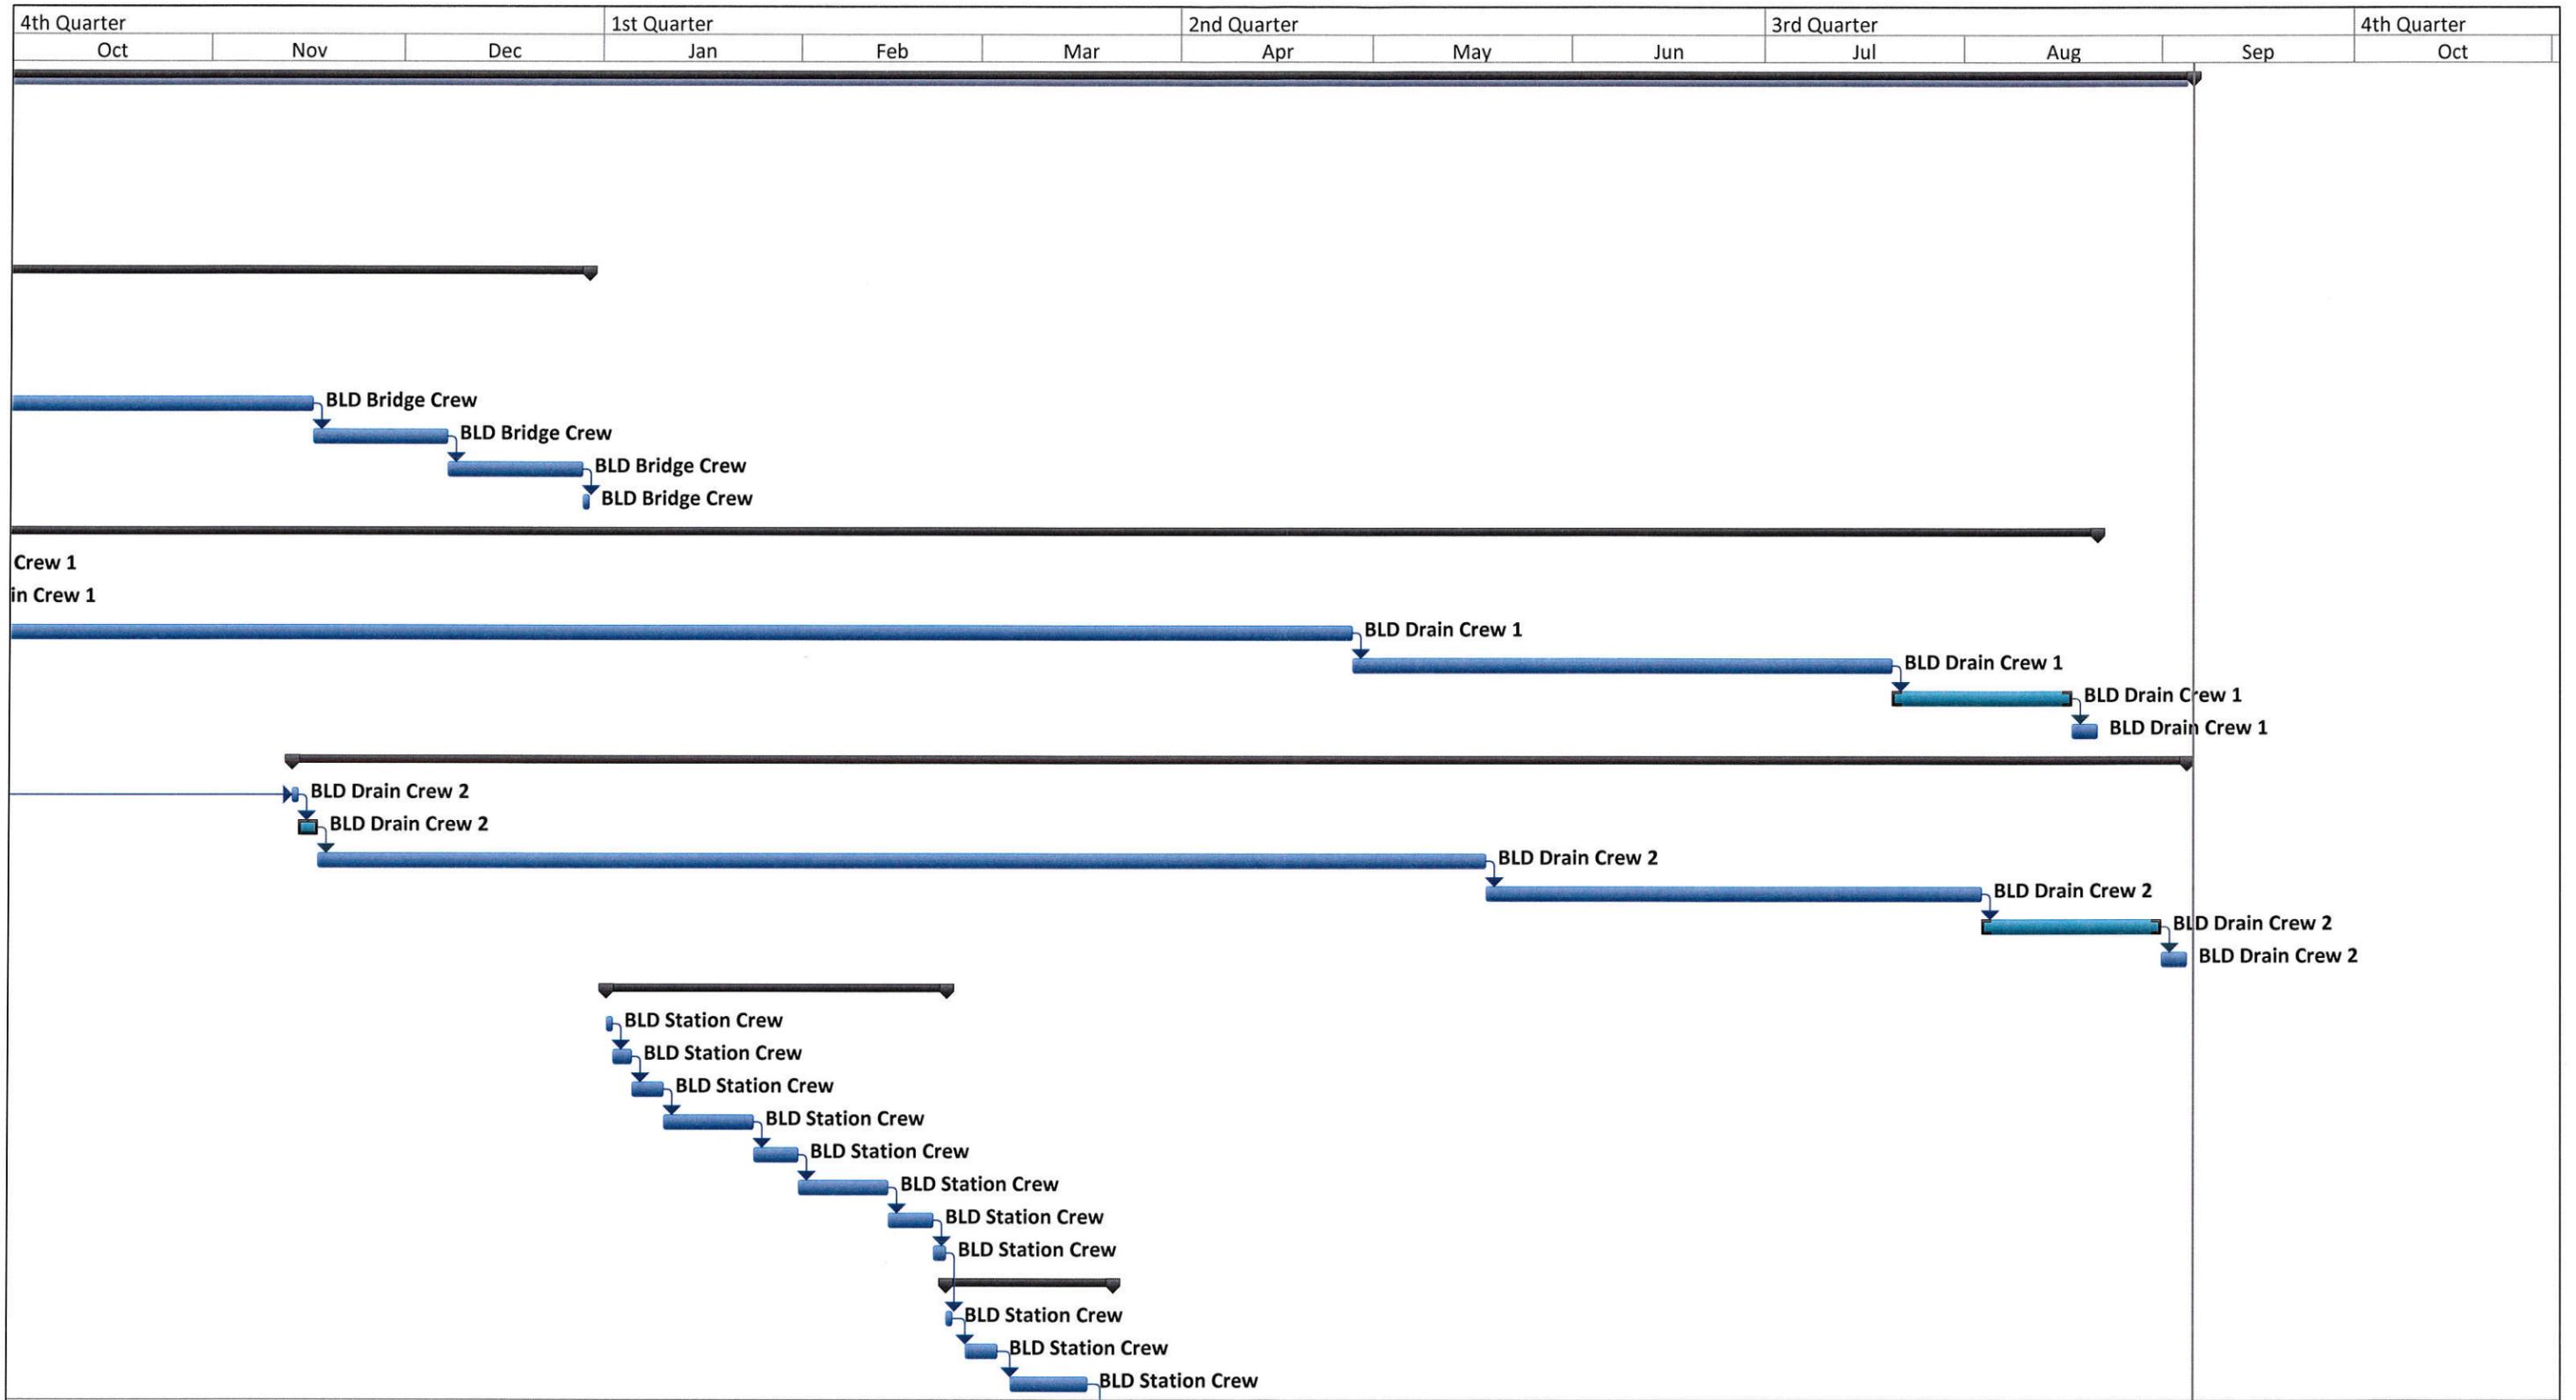

Project: Submitted Palmisano Dra Date: Wed 5/18/16	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Progress	
	Milestone		External Milestone		Manual Task		Start-only			
	Summary		Inactive Task		Duration-only		Finish-only			



Project: Submitted Palmisano Dra
Date: Wed 5/18/16

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			
